

What happened? (activities made since the last follow up)

- * Testing plan #1 Elaboration
- * Culmination of the Registration functionality
- * Public and User Home News/ Dealer panel news implementation
- * Partial login/logout functionality (Ajax facilities has to be included)
- * Poll functionality
- * Partial Meeting Agenda functionality
- * Marketing Actions functionality
- * 50% Mailings functionality

What should have happened? (activities until the follow up date)


- * Site's Template and login facilities culmination: Ajax implementation for the wi3 login/logout module and Firefox considerations for the interface.

Areas of attention

- * Login/logout adjustments
- * Final Approval of the Requirements Specifications (Reviewed Version 17-Nov-2006 send by email to Arne Postma)

What are the next activities? (Tasks and responsibilities)

- * Interface Adjustments. Person in charge: GWT 27 Nov 2006
- * Adjustments in relation with the test's results. Person in charge: GWT 01 Dic 2006
- * Site's Template and login facilities culmination. Person in charge: GWT 30 Nov 2006
- * Testing Plan #2 Elaboration. Person in charge: GWT 28 Nov 2006
- * Execution of the second group of tests. Person in charge: Tierra 29-Nov to 01 -Dic
- * Execution of the programmed activities (According to the plan)

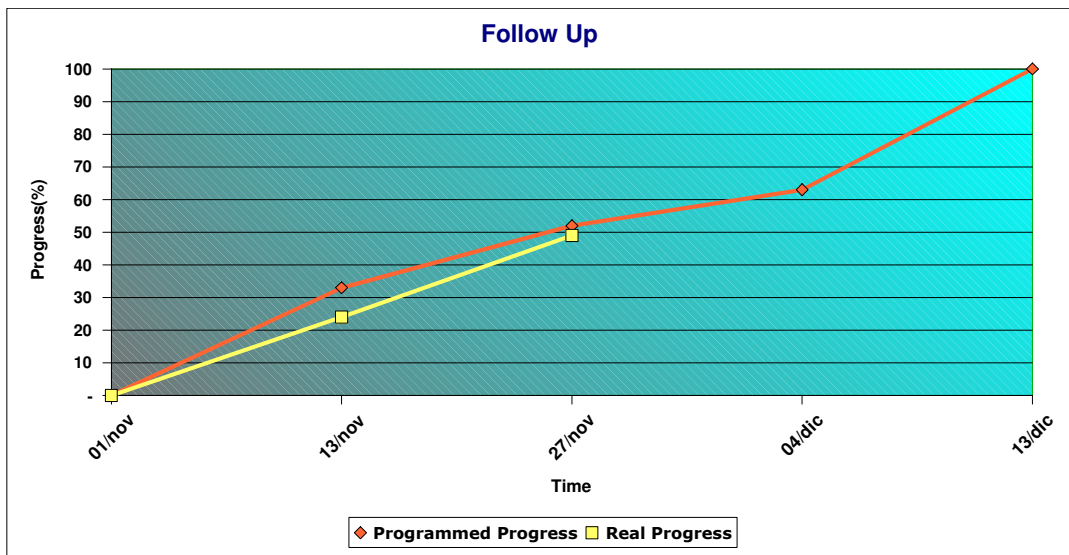

Date	1-nov	13-nov	27-nov	4-dic	13-dic
Programmed	0,00	33,00	52,00	63,00	100,00
Real	0,00	24,00	49,00	0,00	0,00

Legend	
●	Deviation <= 5%
●	Deviation > 5% y Deviation <= 10%
●	Deviation > 10%

Follow Up	Programmed Progress	Real Progress
01/nov	-	-
13/nov	33,00	24,00
27/nov	52,00	49,00
04/dic	63,00	
13/dic	100,00	
